

Project Name

:

Order Number

:

Location

:




Lift Type

:



Foreman



:

Checklist Prior Testing and Commissioning

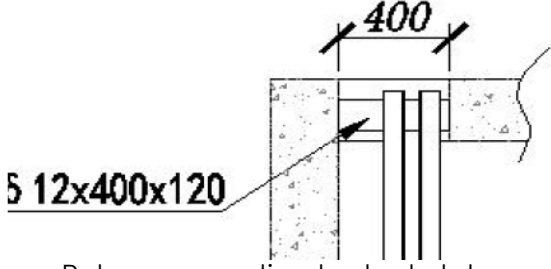
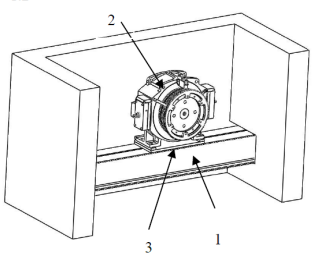
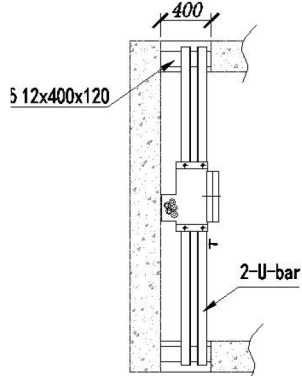
Description of Items to Be Inspected	Accepted? Y/N/NA	Remarks By Foreman	Remarks By QA/QC	Remarks By T&C
With Machine Room (MMR)				
1. Machine Room must free from obstruction and working condition must acceptable				
2. Temporary or permanent lighting must available within Machine Room				
3. Machine Room door must be lockable (Permanent/Temporary)				
4. Power supply for the equipment and grounding system must be acceptable based on the approved specification (Permanent/Temporary)				
5. The transformer, AVR (if included) traction machine and controller must be properly installed based on the installation plan or in the approved location				
6. Steel plate must be installed properly under the bearing beam (concrete shaft) before concrete pouring  Rebar connection to steel plate and bearing beam must be properly installed before concrete pouring (Optional)				
7. Bearing beam must be 20mm longer from the center of the bearing wall and should not less than 75mm embedded from the bearing wall (can be pedestal or wall) 1.1 Machine roomless layout 1.2   1. Bearing beam 2. Traction machine 3. Traction machine baseboard Full weld bearing beam and baseboard				
8. The traction machine cover/guard must properly installed				

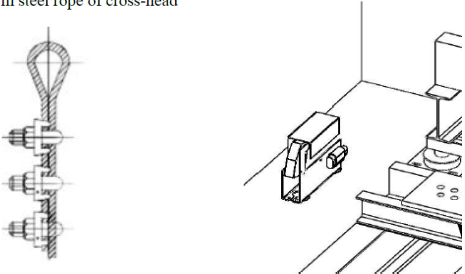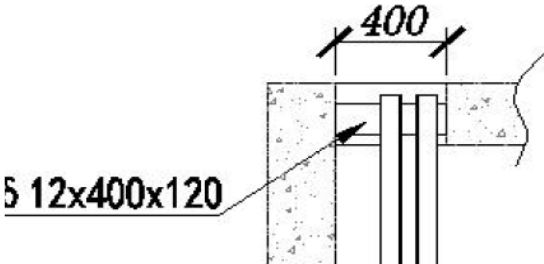




9. The motor manual drive wheel must be properly mounted on the safe area near the traction motor that can easily be access				
10. All welded portions must be quality assured, cleaned and painted				
11. The Traction motor must be lubricated according to specs (If applicable)				
12. The hoisting ropes must properly installed with termination clips/U bolts and 5mm height deference from every rope socket				
13. The speed governor must safely have anchored at MR flooring, sheave vertical deviation must not greater that 5mm, tensioner must be installed at PIT, ropes must have installed in cross-head arc with 3 termination clips and vertical error must not greater than 5mm Drawing arm steel rope of cross-head 				
14. The machine bolt retainers/safety wires must properly installed (if required)				
Machine Room Less (MRL)				
15. Steel plate must be install properly under the bearing beam (concrete shaft) before concrete pouring  400 5 12x400x120 Rebar connection to steel plate and bearing beam must be properly installed before concrete pouring (Optional)				
16. Bearing beam must be 20mm longer from the center of the bearing wall and should not less than 75mm embedded from the bearing wall				

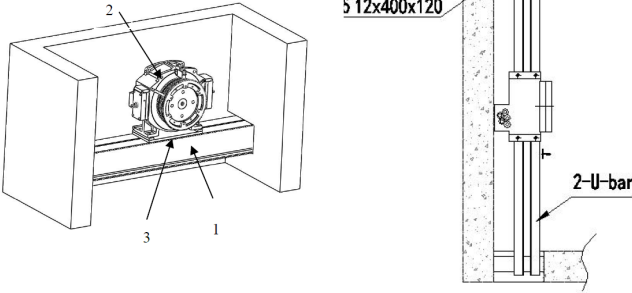1.1 Machine roomless layout 1.2  1. Bearing beam 2. Traction machine 3. Traction machine baseboard Full weld bearing beam and baseboard				
17. The clearances of machine support from the finished floor must complied to the installation plan				
18. The transformer, AVR (if included) traction machine and controller must be properly installed based on the approved installation location				
19. The power supply for the equipment and grounding system must in accordance the requirement				
20. The hoisting ropes must properly installed with termination clips/U bolts and 5mm height deference from every rope socket				
21. The speed governor must, sheave vertical deviation must not greater than 0.5mm, tensioner must be installed at PIT, ropes must have installed in cross-head arc with 3 termination clips and vertical error must not greater that 5mm Drawing arm steel rope of cross-head  Machine roomless: fix above the main guide 				
Shaft/Hoistway & Landing				
22. The elevator shaft must free from any obstruction				
23. Landing door jambs must be properly installed with supports or brace				
24. Landing door panel must be properly installed without scratches and locks must be properly working				
25. Landing and car sill running clearance and leveling must provisionary equal left and right 30mm (1mm+-) tolerance				
26. Centerline of landing door must be equal to car door				
27. The entrance sill must be 2-5mm higher than the finish flooring				
28. Door bottom panel distance from sill is to be 3-6mm				
29. Door panel space is no more than 1mm over the whole height after it closed				











30. The sill toe guard must be installed				
31. There must be available signage/warning notice in all landing door openings				
32. The travelling cable hanger must properly Installed				
33. The traveling cable must be installed and laid properly without possible coalition between the mechanical moving parts				
34. All welding spots must be cleaned without the presence of flux and properly painted				
35. All grouting works must be properly coordinated				
CAR, MAIN & CWT Rail				
36. Car platform must be provisionally aligned, bolt must properly have tightened and the balancing rod/pin must be installed Car frame side brace and straight beam pull strap assembly  Car frame side brace and car platform assembly 				
37. Car platform and door centerline must be provisionally equal to the landing door				
38. Car panels must properly installed without scratches and bolts must properly tightened				
39. Car ceiling must properly installed and aligned without scratches				
40. Hit bow must be properly installed Machine roomless hit bow assembly  Machine room hit bow assembly 				
41. Car and landing door panel space is no more than 1mm over the whole height after it closed				
42. Car door bottom panel distance from sill is to be 3-6mm				
43. The COP must properly installed				
44. Car top Box must properly installed				
45. Travelling cable arrangement under the platform must be acceptable and presentable				
46. The safety gear must be initially adjusted				
47. The steel wire rope of car door operator must be properly installed and the guiding pulley must be smoothly working				





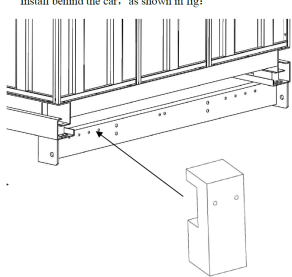
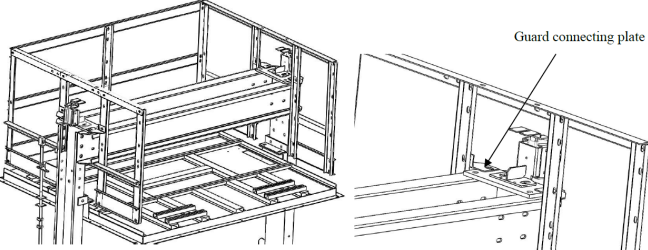


48. All car and CWT guide shoes/rollers must completely and properly have installed and aligned, 10-12mm distance from guide rail with not greater than 1mm deference on both side vertical plane 				
49. The travelling cable hanger under the car must securely installed				
50. The elevator car and counterweight must provisionally balance (Indicate Pieces of CWT initially installed)				
51. The balance block must install properly behind the car 				
52. Door key release must properly functioning (hook engagement depth must not less than 7mm and not greater than 8mm)				
53. Car top barricade must properly have installed according to the manual specification 				
54. The Car apron/toe guard must properly installed				
55. The CWT diversion sheave cover must be properly installed  ※Counterweight filler installation When it is machine roomless, pay attention to make the notched side face to the car side,in order to install the guard. Machine roomless counterweight housingMachine room counterweight housing				
56. CWT lock bracket must be properly installed using the rail clips				

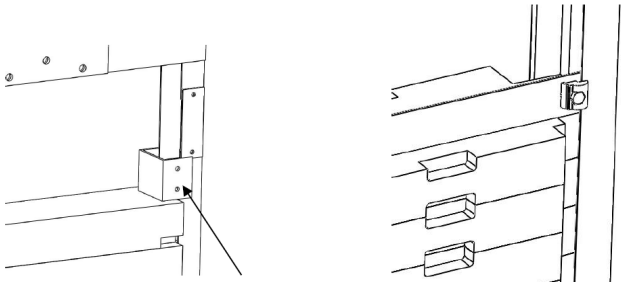

Installation of counterweight plate  Use guide rail clip to fix				
57. The hoisting rope tension must provisionally equal with not greater than 20mm tension				
58. Limit Switch cam must be properly installed opposite side of the governor or in line with the buttons				
Installation of limit switch 				
59. Inductor or leveling switch and leveling board must be provisionally installed with 8 to 12mm operation distance and 0.5 vertical alignment				
Installation view A  Installation view B  Leveling board mode A  Leveling board mode B 				
60. Guide rail bracket for car and ctw 1 st span must be 300-700mm elevated from the finish floor line of PIT, the next bracket span must be simultaneously 2000mm or not greater than 2500mm until reach the last floor with 300mm distance from OH ceiling (double check as per installation drawing requirement). Ensure the quality of welding, welding flux must be removed before the application of paints.				
Car rail brackets  1. Car side connecting angle bar 2. Car side wall angle bar (pedestal) 3. Car rail brackets angle bar Counterweight rail brackets  1. Main support angle bar 2. Counterweight side angle bar 3. Counterweight side wall angle bar(pedestal)				



61. Guide rail plate jointer must be properly tightened the presence of the lock washer ★ Car distortion <0.2mm, sleek>200mm, step<0.03mm ★ Car distortion<0.4mm, sleek>150mm, step<0.10mm ★ Car guide gauge deviation: 0—+2mm ★ Counterweight guide gauge deviation: 0—+3mm   Car guide gusset assembly Counter weight guide gusset assembly				
62. Guide rail must have at least 2 sets of brackets on every span.				
63. Guide rail alignment/straightness must not greater than 5mm				
64. Guide rail clips must be properly tightened with the presence of the lock washer and shim/spacer for the adjustment purposes				
65. All connecting parts with the provision of bolts must properly tightened				
66. All connecting parts with the provision of welding must properly cleaned and painted without flux				
Elevator PIT				
67. The pit buffers must properly have installed, aligned at the center of Car & CWT bottom frame and properly leveled to the PIT flooring with no more than 2mm height deference from the others    External reset switch, switch installed vertically The built-in reset switch, horizontal installation type The buffer can be directly fixed on the ground with expansion bolts, and can also be fixed on the buffer base, the installation height depending on the actual				
68. Buffer distance from car and CWT is not less than 200mm (check as per plan)				
69. The pit must free from debris and water. It must be water proofed				
70. If any, The compensating device or rollers must installed properly				
71. The governor pulley and tensioner must installed properly and safety circuit must function correctly				
72. The CWT cover must be installed not higher than 300mm from pit flooring  ※Installation of counterweight guard Connect to the counterweight guard frame and the guard bulkhead, and use the guide rail clip to fasten the guard frame. Counterweight frame must be installed not higher than 300mm from the pit to 2500mm.				
73. The pit ladder must correctly and safety installed				



General Comments:

This image shows a single sheet of white paper with horizontal blue or grey ruling lines. The lines are evenly spaced and run across the width of the page. There are approximately 20 lines visible. The paper appears to be a standard notebook page or a sheet of stationery.

Date: _____

Date: _____

Date: _____
